









































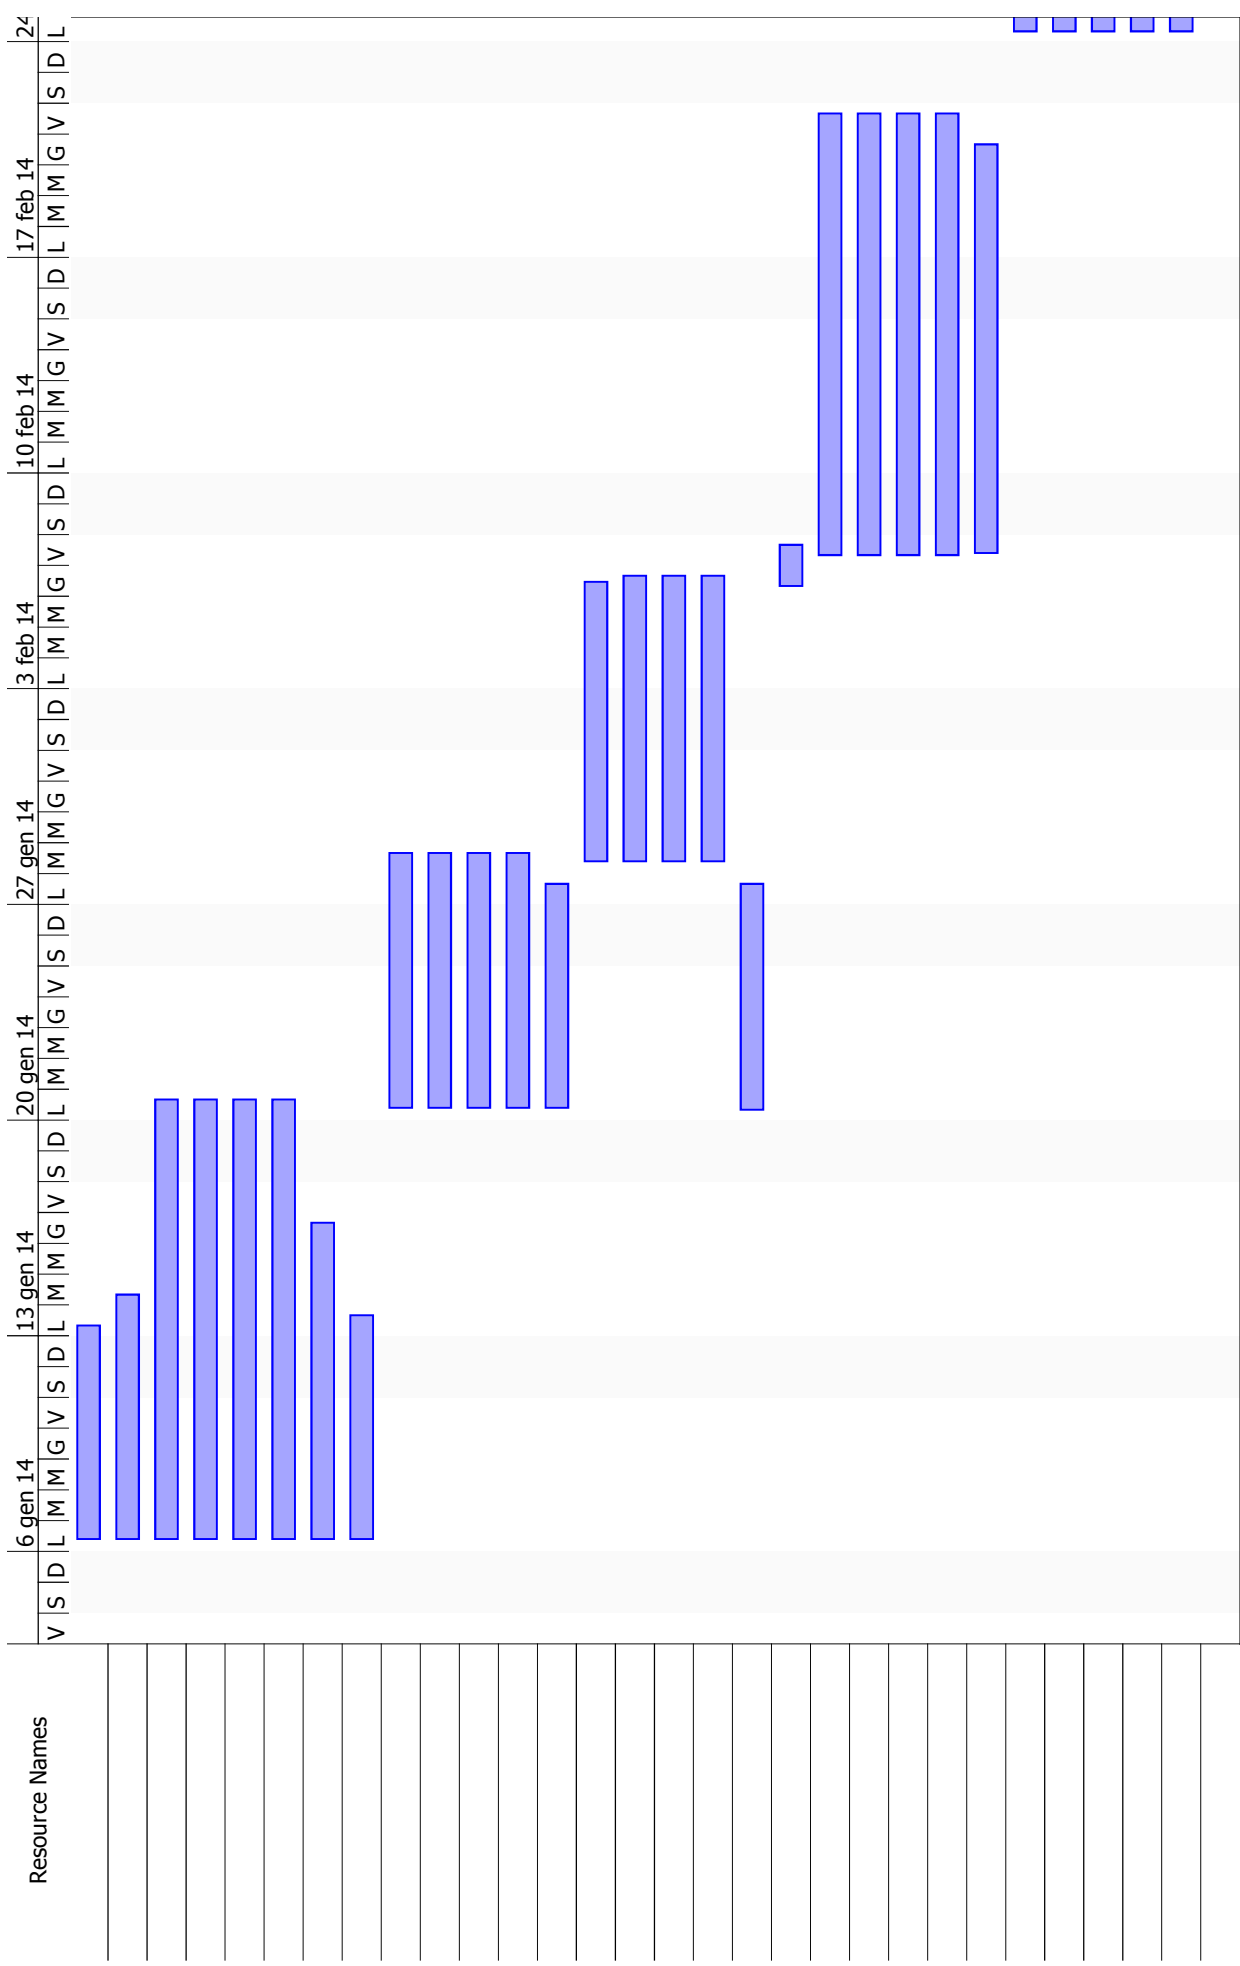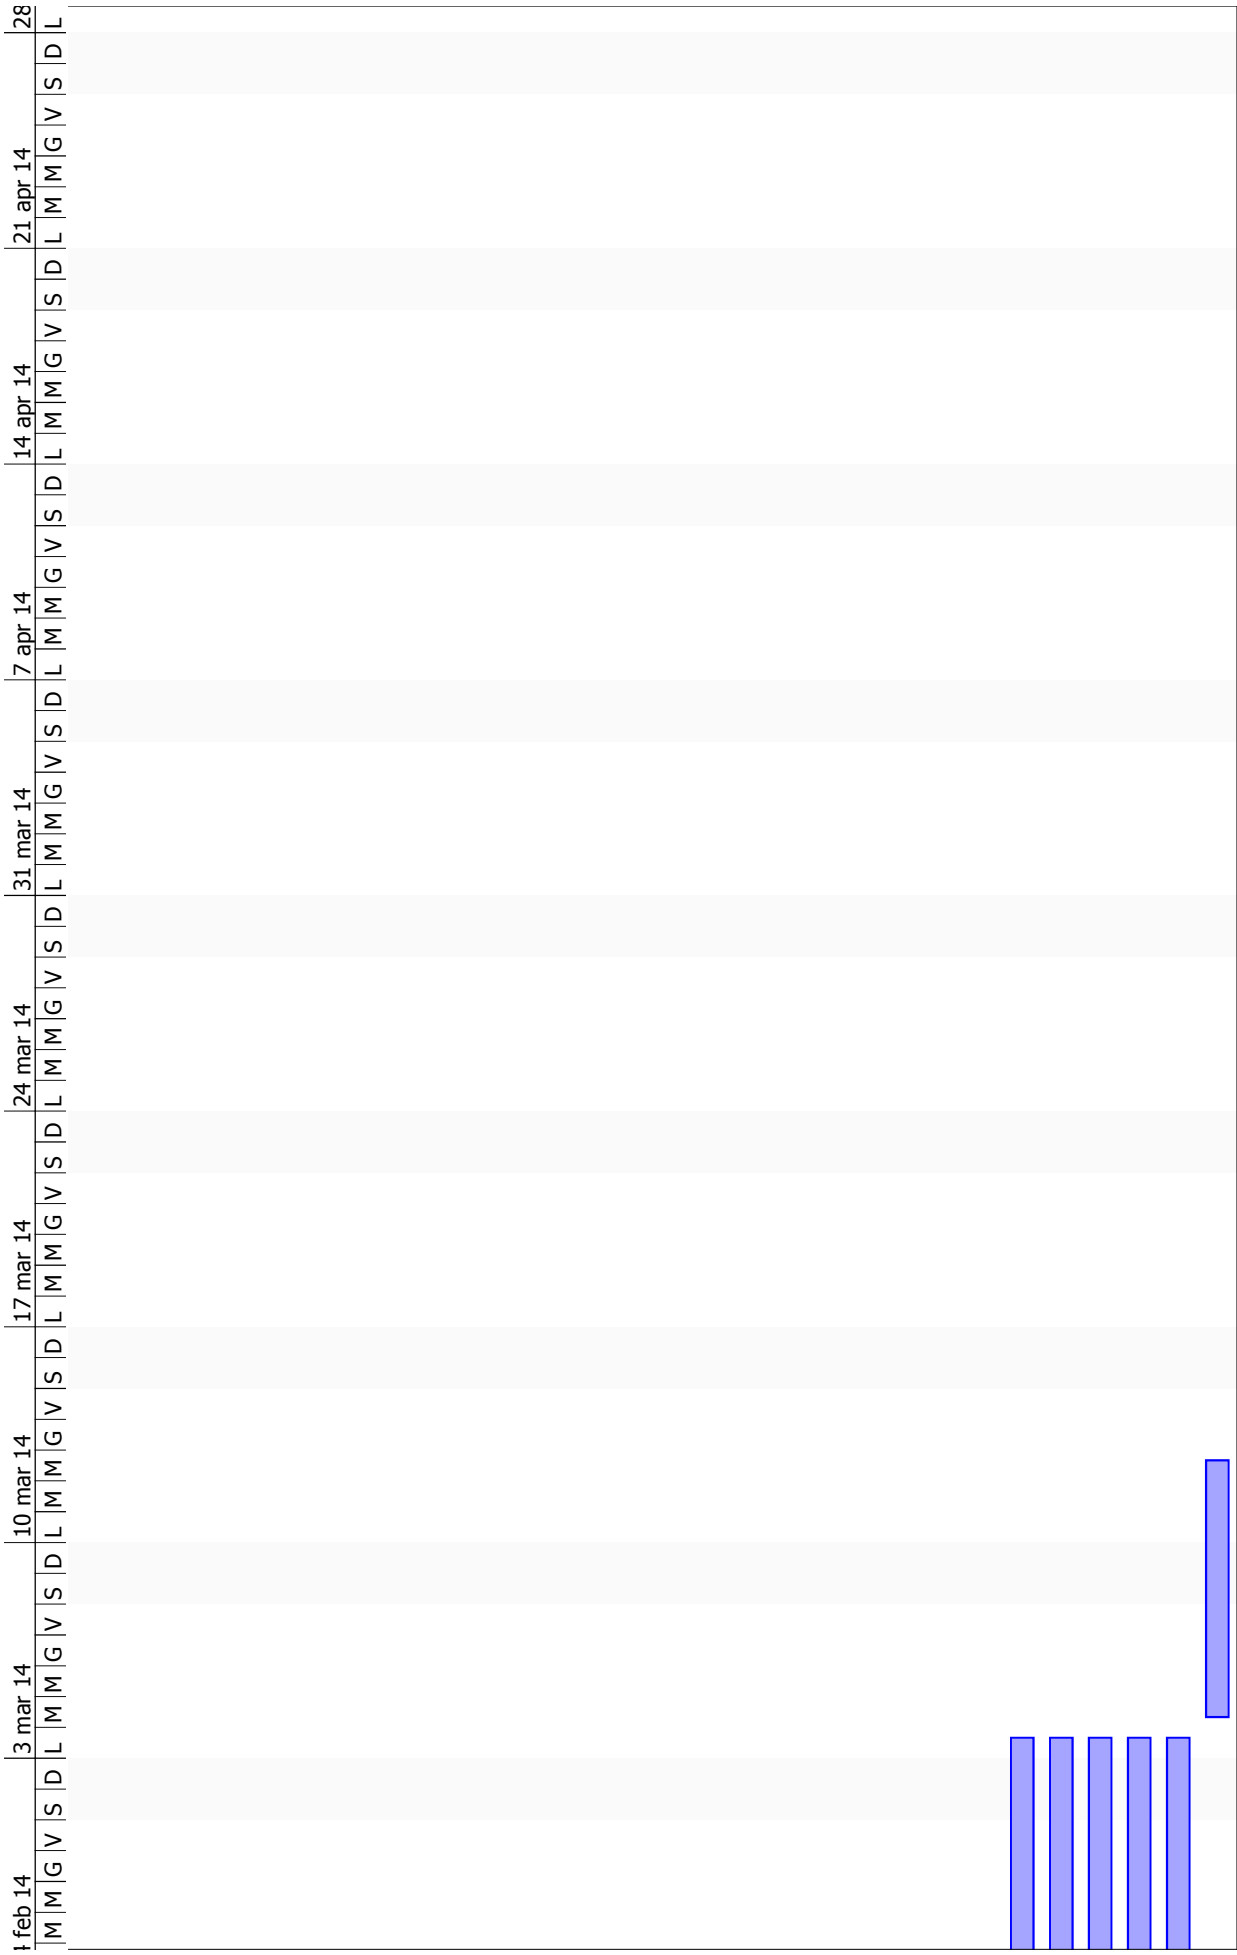




















	Name	Duration	Start	Finish	Predecessors
1		f.e.p. centrale riv. edif.A -rif. 1/vari	5 days	06/01/14 9.00	13/01/14 9.00	
2		f.e.p sistema rack Diffusione Sonora EVAC- rif.54-55-56...	6 days?	06/01/14 9.00	14/01/14 9.00	
3		f.e.p. tubazioni riv. edif. A - P.C. - rif25-26-27-28	10,875 days	06/01/14 9.00	20/01/14 17.00	
4		f.e.p. tubazioni riv. edif. A - P.T. - rif25-26-27-28	10,875 days	06/01/14 9.00	20/01/14 17.00	
5		f.e.p. tubazioni riv. edif. A - P.1. - rif25-26-27-28	10,875 days	06/01/14 9.00	20/01/14 17.00	
6		f.e.p. tubazioni riv. edif. A - P.2. - rif25-26-27-28	10,875 days	06/01/14 9.00	20/01/14 17.00	
7		f.e.p. tubazioni evac edif. A - P.c/t/1/2. - rif62/63/vari	8,875 days	06/01/14 9.00	16/01/14 17.00	
8		f.e.p. canale riv. edif. A - rif29-30-64-65	5,875 days	06/01/14 9.00	13/01/14 17.00	
9		f.e.p. conduttori riv. edif. A - P.C. - rif31-32-33-34-36	6,875 days	20/01/14 9.00	28/01/14 17.00	
10		f.e.p. conduttori riv. edif. A - P.T. - rif31-32-33-34-36	6,875 days	20/01/14 9.00	28/01/14 17.00	
11		f.e.p. conduttori riv. edif. A - P.1. - rif31-32-33-34-36	6,875 days	20/01/14 9.00	28/01/14 17.00	
12		f.e.p. conduttori riv. edif. A - P.2. - rif31-32-33-34-36	6,875 days	20/01/14 9.00	28/01/14 17.00	
13		f.e.p. conduttori evac edif. A - P.c/t/1/2. - rif58/59/60/...	5,875 days	20/01/14 9.00	27/01/14 17.00	
14		f.e.p. componenti in campo- edif. A - P.C.	7,375 days	28/01/14 9.00	06/02/14 13.00	
15		f.e.p. componenti in campo- edif. A - P.T.	7,875 days	28/01/14 9.00	06/02/14 17.00	
16		f.e.p. componenti in campo- edif. A - P.1.	7,875 days	28/01/14 9.00	06/02/14 17.00	
17		f.e.p. componenti in campo- edif. A - P.2.	7,875 days	28/01/14 9.00	06/02/14 17.00	
18		f.e.p. componenti in campi evac edif. A - P.c/t/1/2. - ri...	6 days	20/01/14 8.00	27/01/14 17.00	
19		Programmazione centrale riv. edif. A - P.C./T./1/2	2 days	06/02/14 8.00	07/02/14 17.00	
20		f.e.p. tubazioni riv. edif. A - P.3. - rif25-26-27-28	11 days	07/02/14 8.00	21/02/14 17.00	
21		f.e.p. tubazioni riv. edif. A - P.4. - rif25-26-27-28	11 days	07/02/14 8.00	21/02/14 17.00	
22		f.e.p. tubazioni riv. edif. A - P.5. - rif25-26-27-28	11 days	07/02/14 8.00	21/02/14 17.00	
23		f.e.p. tubazioni riv. edif. A - P.6. - rif25-26-27-28	11 days	07/02/14 8.00	21/02/14 17.00	
24		f.e.p. tubazioni evac edif. A - P.3/4/6/6-rif62/63/vari	9,75 days	07/02/14 10.00	20/02/14 17.00	
25		f.e.p. conduttori riv. edif. A - P.3. - rif31-32-33-34-36	6 days	24/02/14 8.00	03/03/14 17.00	
26		f.e.p. conduttori riv. edif. A - P.4. - rif31-32-33-34-36	6 days	24/02/14 8.00	03/03/14 17.00	
27		f.e.p. conduttori riv. edif. A - P.5. - rif31-32-33-34-36	6 days	24/02/14 8.00	03/03/14 17.00	
28		f.e.p. conduttori riv. edif. A - P.6. - rif31-32-33-34-36	6 days	24/02/14 8.00	03/03/14 17.00	
29		f.e.p. conduttori evac edif. A - P.c/t/1/2. - rif58/59/60/...	6 days	24/02/14 8.00	03/03/14 17.00	
30		f.e.p. componenti in campo- edif. A - P.3.	7 days	04/03/14 8.00	12/03/14 17.00	






























giu 14							7 lug 14							14 lug 14						
M	M	G	V	S	D	L	M	M	G	V	S	D	L	M	M	G	V	S	D	L

		Name	Duration	Start	Finish	Predecessors
31		f.e.p. componenti in campo- edif. A - P.4.	7 days	04/03/14 8.00	12/03/14 17.00	
32		f.e.p. componenti in campo- edif. A - P.5.	7 days	04/03/14 8.00	12/03/14 17.00	
33		f.e.p. componenti in campo- edif. A - P.6.	7 days	04/03/14 8.00	12/03/14 17.00	
34		f.e.p. componenti in campo evac edif. A - P.3/4/5/6. - r...	6,625 days	04/03/14 11.00	12/03/14 17.00	
35		Programmazione centrale riv. edif. A - P.3./4./5/6	2 days	13/03/14 8.00	14/03/14 17.00	
36		Cartellonistica, etichettature, test, aggiornamento piani...	6 days	17/03/14 8.00	24/03/14 17.00	
37		Verifica sistema rivelazione incendi - precollauda	3 days	17/03/14 8.00	19/03/14 17.00	
38		Formazione personale	1 day	17/03/14 8.00	17/03/14 17.00	
39		f.e.p. centrale riv. edif.B -rif. 2/vari	4 days	18/03/14 8.00	21/03/14 17.00	
40		f.e.p. tubazioni riv. edif. B - P.C. - rif25-26-27-28	9 days	18/03/14 8.00	28/03/14 17.00	
41		f.e.p. tubazioni riv. edif. B - P.T. - rif25-26-27-28	6 days	29/03/14 8.00	07/04/14 17.00	
42		f.e.p. tubazioni riv. edif. B - P.T. - rif25-26-27-28	15 days	18/03/14 8.00	07/04/14 17.00	
43		f.e.p. tubazioni riv. edif. B - P.1. - rif25-26-27-28	15 days	18/03/14 8.00	07/04/14 17.00	
44		f.e.p. tubazioni riv. edif. B - P.2. - rif25-26-27-28	13 days	18/03/14 8.00	03/04/14 17.00	
45		f.e.p. tubazioni evac edif. B - P.c/t/1/2. - rif62/63/vari	20 days	18/03/14 8.00	14/04/14 17.00	
46		f.e.p. conduttori riv. edif. B - P.C. - rif31-32-33-34-36	5 days	08/04/14 8.00	14/04/14 17.00	
47		f.e.p. conduttori riv. edif. B - P.T. - rif31-32-33-34-36	15 days	08/04/14 8.00	28/04/14 17.00	
48		f.e.p. conduttori riv. edif. B - P.1. - rif31-32-33-34-36	10 days	08/04/14 8.00	21/04/14 17.00	
49		f.e.p. conduttori riv. edif. B - P.2. - rif31-32-33-34-36	6 days	08/04/14 8.00	15/04/14 17.00	
50		f.e.p. conduttori evac edif. B - P.c/t/1/2. - rif58/59/60/...	10 days	08/04/14 8.00	21/04/14 17.00	
51		f.e.p. componenti in campo- edif. B - P.C.	7 days	21/04/14 8.00	29/04/14 17.00	
52		f.e.p. componenti in campo- edif. B - P.T.	14 days	21/04/14 8.00	08/05/14 17.00	
53		f.e.p. componenti in campo- edif. B - P.T.	8 days	29/04/14 8.00	08/05/14 17.00	
54		f.e.p. componenti in campo- edif. B - P.1.	14 days	21/04/14 8.00	08/05/14 17.00	
55		f.e.p. componenti in campo- edif. B - P.2.	10 days	21/04/14 8.00	02/05/14 17.00	
56		f.e.p. componenti in campo evac edif. B - P.c/t/1/2. - ri...	14 days	21/04/14 8.00	08/05/14 17.00	
57		Programmazione centrale riv. edif. B - P.C./T./1/2	2 days	08/05/14 8.00	09/05/14 17.00	
58		Cartellonistica, etichettature, test, aggiornamento piani...	6 days	05/05/14 15.00	13/05/14 15.00	
59		Verifica sistema rivelazione incendi - precollauda	2 days	10/05/14 8.00	13/05/14 17.00	
60		f.e.p. centrale riv. edif.C -rif. 3/vari	2 days	14/05/14 8.00	15/05/14 17.00	



giu 14							7 lug 14							14 lug 14						
M	M	G	V	S	D	L	M	M	G	V	S	D	L	M	M	G	V	S	D	L

		Name	Duration	Start	Finish	Predecessors
61		f.e.p. tubazioni riv. edif. C - P.T./1 - rif25-26-27-28	10 days	16/05/14 8.00	29/05/14 17.00	
62		f.e.p. conduttori riv. edif. C - P.T./1 - rif31-32-33-34-36	10 days	16/05/14 8.00	29/05/14 17.00	
63		f.e.p. componenti in campo- edif. C - P.T./1	6 days	29/05/14 8.00	05/06/14 17.00	
64		Cartellonistica, etichettature, test, aggiornamento piani...	2 days	06/06/14 8.00	09/06/14 17.00	
65		Verifica sistema rivelazione incendi - precollaudo	1 day	10/06/14 8.00	10/06/14 17.00	
66		f.e.p. centrale riv. edif.D -rif. 3/vari	2 days	14/05/14 8.00	15/05/14 17.00	
67		f.e.p. tubazioni riv. edif. D - P.T.- rif25-26-27-28	5 days	16/05/14 8.00	22/05/14 17.00	
68		f.e.p. conduttori riv. edif. D - P.T. - rif31-32-33-34-36	5 days	16/05/14 8.00	22/05/14 17.00	
69		f.e.p. componenti in campo- edif. D - P.T.	3 days	23/05/14 8.00	27/05/14 17.00	
70		Cartellonistica, etichettature, test, aggiornamento piani...	2 days	26/05/14 8.00	27/05/14 17.00	
71		Verifica sistema rivelazione incendi - precollaudo	1 day	27/05/14 8.00	27/05/14 17.00	
72		f.e.p. centrale riv. edif.E-8 -rif. 3/vari	2 days	14/05/14 8.00	15/05/14 17.00	
73		f.e.p. tubazioni riv. edif. E-8 - P.T./P.C.- rif25-26-27-28	10 days	16/05/14 8.00	29/05/14 17.00	
74		f.e.p. conduttori riv. edif. E-8 .T./P.C. - rif31-32-33-34-36	10 days	16/05/14 8.00	29/05/14 17.00	
75		f.e.p. componenti in campo- edif. E-8 - P.T./P.C.	5 days	30/05/14 8.00	05/06/14 17.00	
76		Cartellonistica, etichettature, test, aggiornamento piani...	2 days	06/06/14 8.00	09/06/14 17.00	
77		Verifica sistema rivelazione incendi - precollaudo	1 day	09/06/14 8.00	09/06/14 17.00	
78		f.e.p. centrale riv. edif.F -rif. 3/vari	2 days	14/05/14 8.00	15/05/14 17.00	
79		f.e.p. tubazioni riv. edif. F - P.T./1 - rif25-26-27-28	10 days	16/05/14 8.00	29/05/14 17.00	
80		f.e.p. conduttori riv. edif. F - P.T./1 - rif31-32-33-34-36	10 days	16/05/14 8.00	29/05/14 17.00	
81		f.e.p. componenti in campo- edif. F - P.T./1	6 days	29/05/14 8.00	05/06/14 17.00	
82		Cartellonistica, etichettature, test, aggiornamento piani...	2 days	06/06/14 8.00	09/06/14 17.00	
83		Verifica sistema rivelazione incendi - precollaudo	1 day	10/06/14 8.00	10/06/14 17.00	
84		IMPREVISTI	5 days	11/06/14 8.00	17/06/14 17.00	

giu 14			7 lug 14			14 lug 14								
M	G	V	S	D	L	M	G	V	S	D	L	M	M	G
